


Oyster Management Areas – Sanctuaries: Tred Avon

Restoration Sites in the Tred Avon River

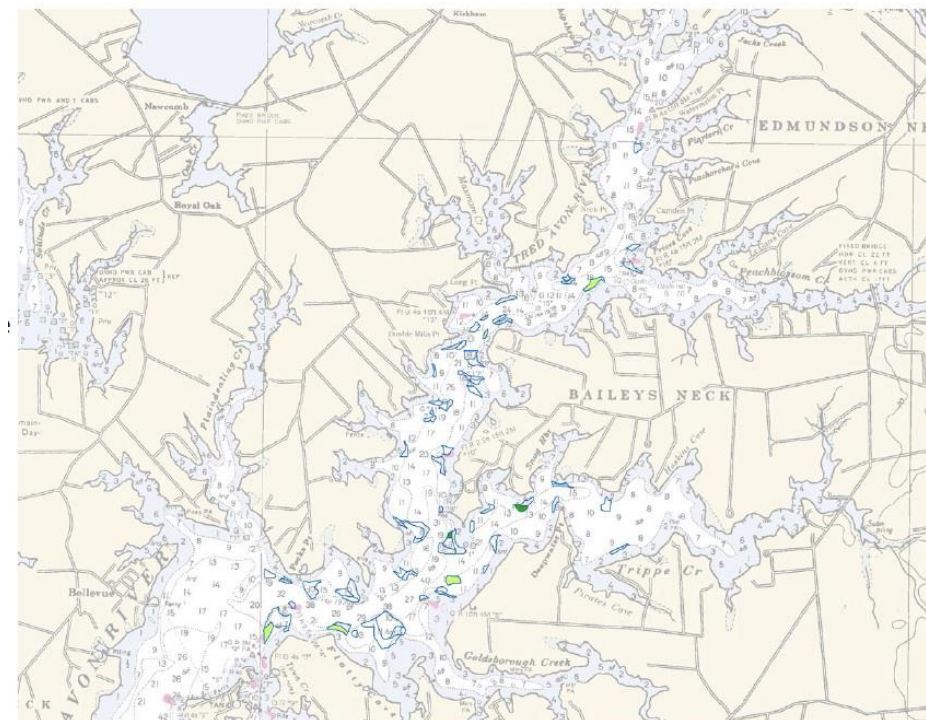

Initial restoration
complete

Initial restoration
partly complete

Planned
restoration

Restoration Plan:

- 147 acres to be restored
- 666.1 million spat to be planted
- 119,499 cubic yards of reef building substrate to be planted

Current Status (2015):

- 2.6 acres have been constructed
- 16 acres have been partially constructed
- 10.18 million spat already planted
- 8 acres to be constructed delayed
- Environmental Assessment for shallow water construction underway

Tred Avon Oyster Restoration Status as of 2015

